RENDEZVOUS DOCKING FACILITY - Proj. 3428

FEB. 1963

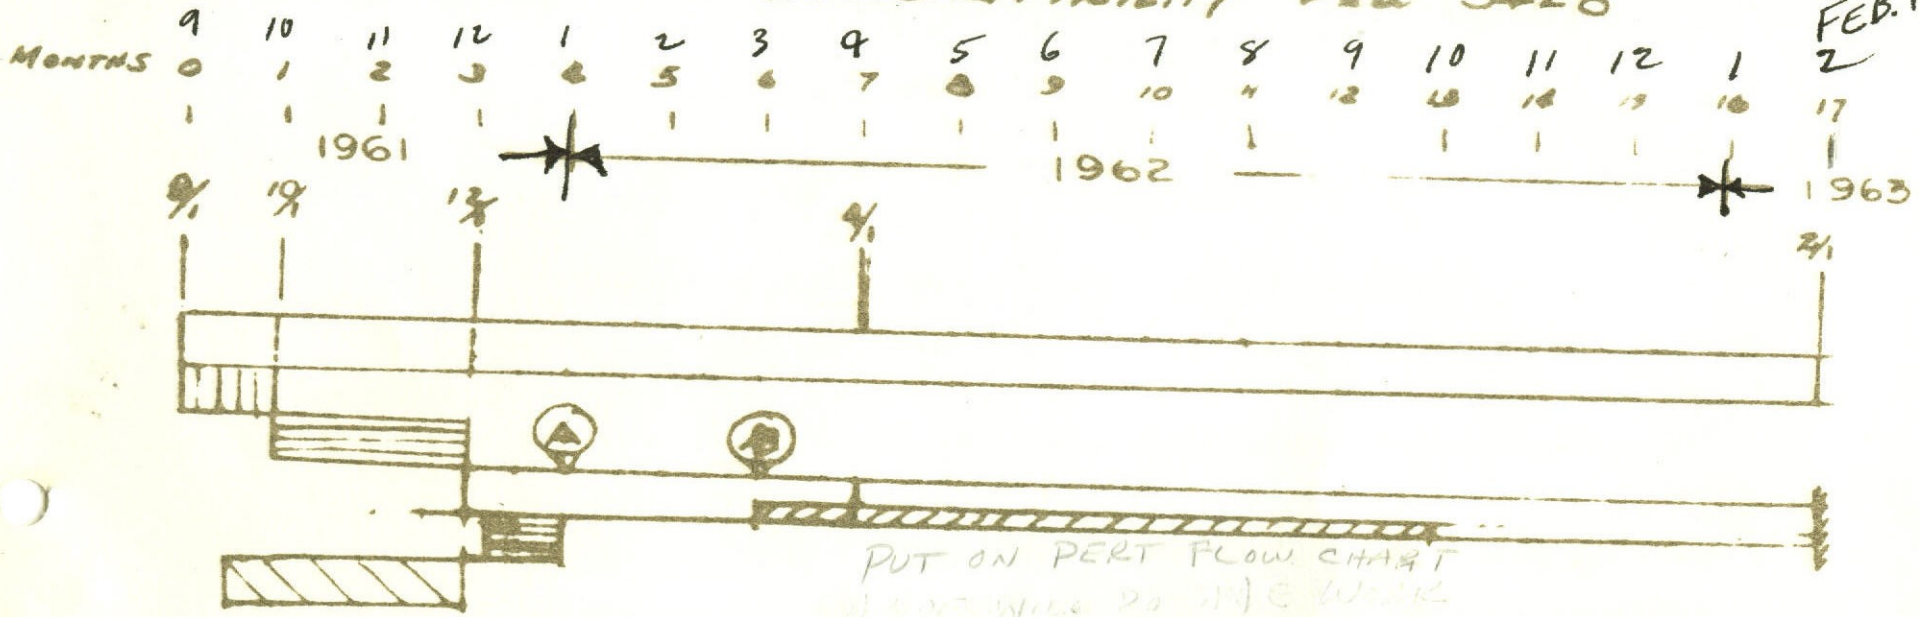

0-1 Mos. - LRC - Perf. & Des Specs Complete

1-3 Mos - LRC - Procurement Cycle

3-7 Mos - Cont. - Final Des Complete

6-13 Mos. Cont. - Purch & Deliv of Comp.

13-17 Mos Cont - Installation & Checkout Comp

Purch. to start @ 9/1/62 Sufficient Des Accompl.
Close monitoring req'd - No liquidated damages.

½ -3 Mos. - A-E/LRC Task Order - Investig. Trusses.

1½ -4 Mos. Contract Change Negotiation Period

@ 4 Mos. Change Order

Const Specs	9-24-61
Procurement	10-1-61
ADV.	10-8-61
Bid Open	11-24-61
Award	12-1-61
App'd by LRC	4-1-62
	10-1-62
	2-1-63
Start	9-15-61
Comp.	12-5-61
Start	12-8-61
	1-1-62

BEHIND

9-1-61
